

# **Arlington High School Building Project**

AHS Construction Update - 5/7/20

### Arlington HS Construction Schedule: April 20, 2020 – April 2025


#### **Construction Details**

Sitework required to prepare for future construction of the new Arlington HS began in April. Work areas during this phase include the front green, the Peirce practice field and the current softball field and adjacent basketball court. Construction work hours will be Monday through Friday and follow local bylaws. Overtime and Saturday work may be required as the schedule develops. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

#### COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

## PHASE 1 SITEWORK (May 2020 - June 2020)

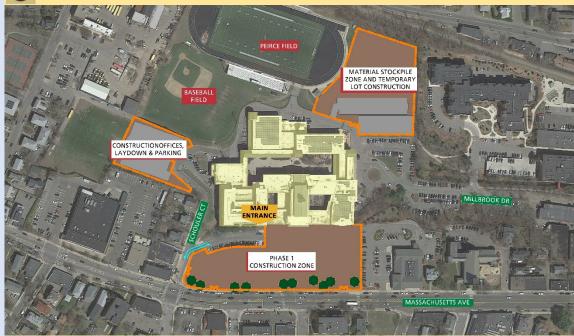

#### Construction Look Ahead – Week of May 11, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### **Public Way Impacts**

Mass Ave entrance and circular drive closed - district offices will be accessible by the Fusco Building Entrance through Schouler Court

#### **Interior Site Activities**

None currently

#### **General Site Activities**

- Installation of remaining construction fence & scrim
- Removal of tree stumps Mass Ave Front lawn / west parking
- Salvage of Mass Ave lawn memorials
- Removal and stock piling of topsoil lower construction lot
- Reworking basketball court into parking

#### **Weekend Work**

None at this time

Sign up for Weekly Construction Updates: https://ahsbuilding.org/news/construction-updates/. For more information, visit: www.ahsbuilding.org. Email questions or concerns to: ahsbuilding@arlington.k12.ma.us. For immediate, on-site assistance contact Hal Raymond,

Skanska Site Representative, (617) 352-8593.





