



Arlington High School Building Project

AHS Construction Update – 6/18/20


Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details

Sitework required to prepare for future construction of the new Arlington HS began in April. Work areas during this phase include the front green, the Peirce practice field and the current softball field and adjacent basketball court. Construction work hours will be Monday through Friday and follow local bylaws. Overtime and Saturday work may be required as the schedule develops. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

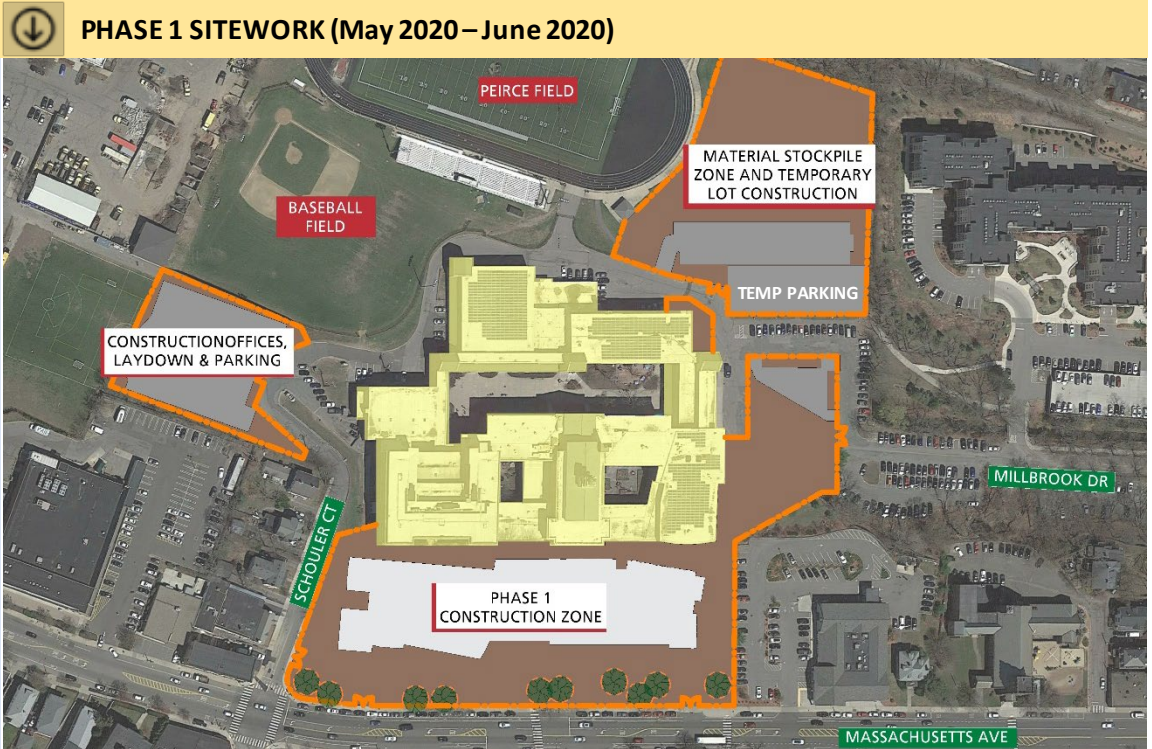

Construction Look Ahead – Week of June 22, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Mass Ave entrance and circular drive closed

Interior Site Activities

- Framing of temporary phasing swing space

General Site Activities

- Schouler Court:
 - Water tie-in work on hold until further notice
- Mass Ave Front Lawn:
 - Removal of top-soil and pavement
 - Installation of drainage line
 - Pre-excavation for support of excavation (SOE)
 - Installation of temporary gas line to Fusco building
- West Parking Lot:
 - Underground electrical service installation
- New Temporary Parking Lot:
 - Complete

Weekend Work

- None at this time

Sign up for Weekly Construction Updates <https://ahsbuilding.org/news/construction-updates/>

For more information, visit: www.ahsbuilding.org

Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

**For immediate, on-site assistance contact Hal Raymond,
Skanska Site Representative. (617) 352-8593**



ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JUNE 22, 2020

Progress Photos as of (6/16/20)



Photograph 1: Derenzo assembling 36in drain-pipe for installation in the front lawn area (6/15/20)



Photograph 2: Costello Demolition Crew removing the fire escape from the Auditorium building (6/8/20)



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JUNE 22, 2020

Progress Photos as of (6/16/20)



Photograph 2: J. Derenzo scraping turf adhesive off the playground area in preparation for new parking (6/9/20)



Photograph 3: Costello demolition crew ripping off the canopy to the main entrance (6/9/20)



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JUNE 22, 2020

Progress Photos as of (6/16/20)



Photograph 4: Derenzo opened up schooler court to install a new water tie in for a new sprinkler line (6/11/20)
