



# Arlington High School Building Project

AHS Construction Update – 7/2/20

## Arlington HS Construction Schedule: April 2020 – April 2025

### Construction Details

Sitework required to prepare for future construction of the new Arlington HS began in April. Work areas during this phase include the front green, the Peirce practice field and the current softball field and adjacent basketball court. Construction work hours will be Monday through Friday and follow local bylaws. Overtime and Saturday work may be required as the schedule develops. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

### COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates

<https://ahsbuilding.org/news/construction-updates/>

For more information, visit:


[www.ahsbuilding.org](http://www.ahsbuilding.org)

Email questions or concerns to:

[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

**For immediate, on-site assistance contact**

**Hal Raymond, Skanska Site Representative, (617) 352-8593**

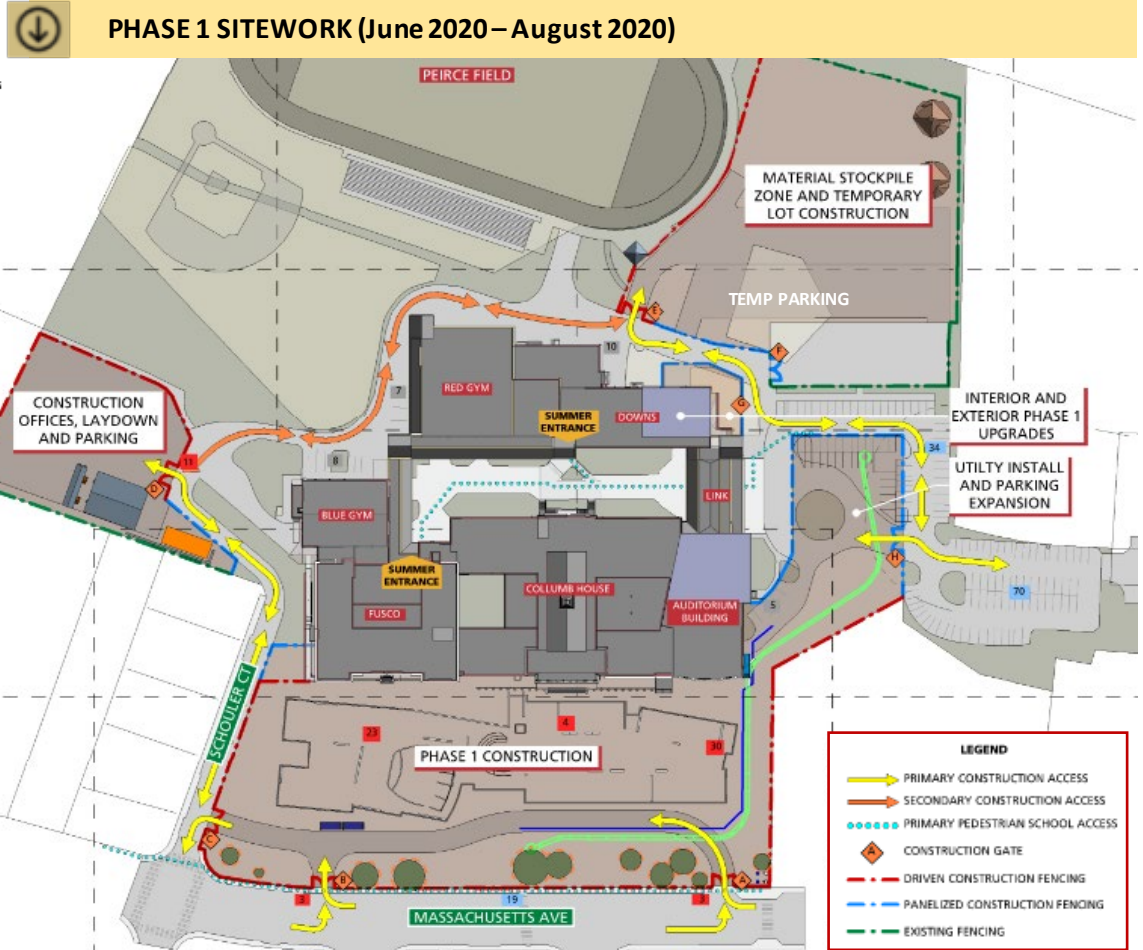

### Construction Look Ahead – Week of July 6, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts

- Mass Ave entrance and circular drive closed
- Schouler Court road excavation work (two-way traffic still accommodated)

#### Interior Site Activities: Phase 1 Interior Temp Phasing

- Finish framing/begin drywall of temporary phasing swing spaces
- Installation of electric & mechanical piping and ducts

#### General Site Activities

- Mass Ave Front Lawn:
  - Removal of top-soil and pavement
  - Installation of drainage line
  - Pre-excavation for support of excavation (SOE)
  - Installation of temporary gas line to Fusco building
  - Installation of new electric lines
- West Parking Lot:
  - Installation of block retaining wall
- Material Stockpile/Temp Construction Lot:
  - Finish grading contractor storage area
- Schouler Court:
  - Water tie-in work (water shutdown – 7/7 & 7/8 during construction hours)
  - Roadway excavation

#### Weekend Work

- None at this time



**CONSIGLI**  
Est. 1905

**ARLINGTON HIGH SCHOOL**

**WEEKLY UPDATE – WEEK OF JULY 6, 2020**

**Progress Photographs as of 06/26/2020**



***Photograph 1: Derenzo installing 48in drain line along Mass Ave (6/26/20)***



***Photograph 2: Derenzo placing concrete for west lot duct bank (6/23/20)***



CONSIGLI  
Est. 1905

**ARLINGTON HIGH SCHOOL**

**WEEKLY UPDATE – WEEK OF JULY 6, 2020**



*Photograph 3: Griffin laying out electrical service for new temporary guidance offices in Downs building (6/26/20)*



*Photograph 4: TJ McCartney framing in the transaction window in Downs building (6/26/20)*



**ARLINGTON HIGH SCHOOL**

**WEEKLY UPDATE – WEEK OF JULY 6, 2020**



*Photograph 2: Griffin working on electrical vault in the ground in front of Fusco Building (6/25/20)*



*Photograph 6: Rustic coring a hole for west fire protection line (6/17/20)*
