

Arlington High School Building Project

AHS Construction Update - 7/9/20

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details


Sitework required to prepare for future construction of the new Arlington HS began in April. Work areas during this phase include the front green, the Peirce practice field and the current softball field and adjacent basketball court. Construction work hours will be Monday through Friday and follow local bylaws. Overtime and Saturday work may be required as the schedule develops. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement. construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates https://ahsbuilding.org/news/const ruction-updates/ For more information, visit: www.ahsbuilding.org Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

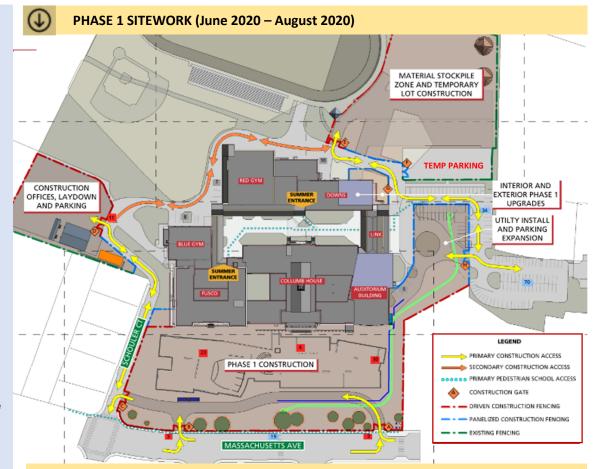

Construction Look Ahead - Week of July 13, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Mass Ave entrance and circular drive closed
- Schouler Court repair of pavement at trench locations (two-way traffic accommodated)
- East side rotary closed turn around in the "temp parking" lot

Interior Site Activities: Phase 1 Interior Temp Phasing

- Drywall installation of temporary phasing swing spaces
- Installation of electric & mechanical piping and ducts

General Site Activities

- Mass Ave Front Lawn:
 - Clock tower balustrade (railing) removal (due to safety concerns)
 - Removal of top-soil and pavement
 - 0 Installation of drainage line
 - Mounting of temporary gas line to Fusco building
 - Installation of new underground electric lines
- West Parking Lot:
 - Installation of block retaining wall
- Material Stockpile/Temp Construction Lot:
 - Finish grading contractor storage area
- Schouler Court:
 - Roadway repair/paving

Weekend Work/Work Hours

- No weekend work at this time
- Work hours temporarily extended 8:00am 6:00pm (in accordance with local bylaws)









WEEKLY UPDATE – WEEK OF JULY 13, 2020

Progress Photographs - Taken Week of 06/29/2020



Photograph 1: Derenzo Installing 8in Water Line in Front Lawn



Photograph 2: Griffin running conduit between electrical and telecom vaults



WEEKLY UPDATE – WEEK OF JULY 13, 2020



Photograph 3: P.J. Kennedy mounting 10in gas line to the front of Fusco Building



Photograph 4: Keller drilling and installing caissons for support of excavation (SOE) in front of Auditorium Building



WEEKLY UPDATE – WEEK OF JULY 13, 2020




Photograph 5: P. J. Kennedy welding segments of 10in gas line together in front of Fusco Building



Photograph 6: Irvine bringing in plumbing for new bathroom in the new swing space at Downs Building



WEEKLY UPDATE – WEEK OF JULY 13, 2020

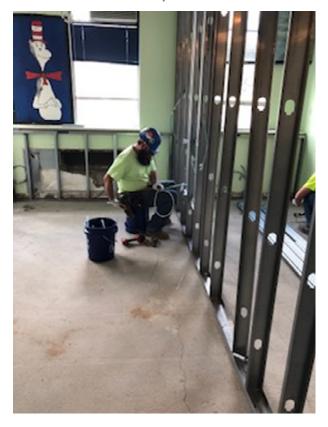

Photograph 7: Electrical work in the new swing space of the Downs Building



Photograph 8: T.J. McCartney framing in the transaction window in the vestibule of the new swing space in Downs Building
