



Arlington High School Building Project

AHS Construction Update – 8/5/20

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details

Sitework and temporary phasing interior work is required to prepare for future construction of the new Arlington HS. Work areas during this phase include the front green, the Peirce practice field, the current softball field, Preschool rotary and adjacent area, Downs House and the Auditorium Building. Construction work hours will be Monday through Friday will and follow local bylaws (8 AM – 6 PM). Saturday work is currently required from Jul-20 thru Aug-20 to maintain the schedule. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

COVID-19 Update


The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
For more information, visit:
www.ahsbuilding.org
Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact
Hal Raymond, Skanska Site Representative, (617) 352-8593



PHASE 1 SITEWORK / TEMPORARY PHASING UPGRADES (June 2020 – August 2020)

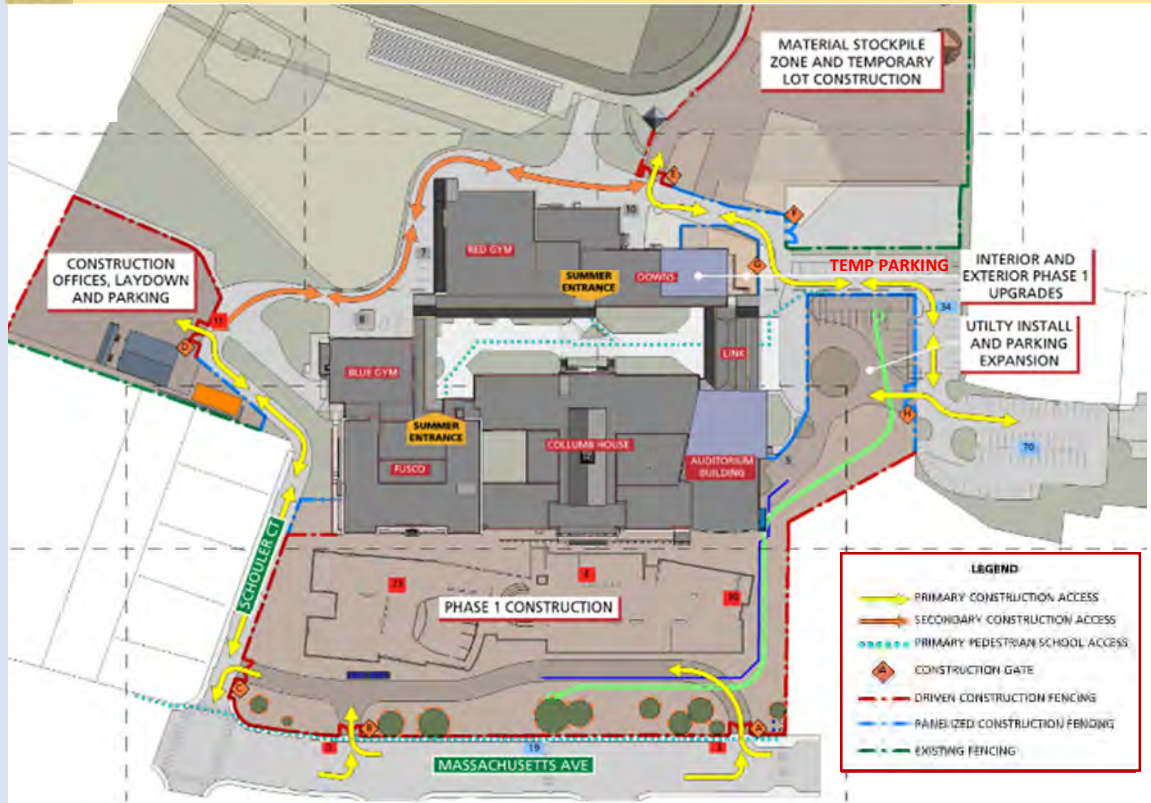

Construction Look Ahead – Week of August 10, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Mass Ave entrance and circular drive closed
- East side rotary closed (turnaround in the "temp parking" lot)

Interior Site Activities: Phase 1 Interior Temp Phasing

- Painting and flooring of temporary phasing swing spaces
- Installation of electric & mechanical and plumbing finishes

General Site Activities

- Mass Ave Front Lawn:
 - Preparation and paving of sidewalk to entrance
 - Installation of support of excavation (SOE)
 - Drilling and installation of Rammed Aggregate Piers (RAPS)
 - Gas meter relocation in front of Fusco
 - Removal of clocktower spindles
- West Parking Lot:
 - Contractor parking
 - Installation of construction trailers
- Material Stockpile/Temp Construction Lot:
 - Paving contractor storage area
- Schouler Court:
 - No work at this time

Weekend Work/Work Hours/Night Work

- Saturday (7/25) – Drilling and installation of support of excavation (SOE) on Mass Ave /Grading at East side rotary
- Work hours temporarily extended 8:00 am – 6:00 pm (in accordance with local bylaws)



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF AUGUST 10, 2020

Progress Photographs – as of 07/27/2020



Photograph 1: Riggs placing and finishing “Deadman Wall” for Support of Excavation (SOE) in Front Lawn



Photograph 2: Keller Vibrating SOE piles in front of school



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF AUGUST 10, 2020



Photograph 3: Derenzo prepping back parking area east of Auditorium building



Photograph 4: Griffin Piping in new panel in Downs building
