



Arlington High School Building Project

AHS Construction Update – 9/3/20

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details

Sitework and temporary phasing work is required to prepare for future construction of the new Arlington HS. Work areas during this phase include the front green, the Peirce practice field, the current softball field. Construction work hours will be Monday through Friday will and follow local bylaws (8 AM – 6 PM). Saturday work may be required to maintain the schedule. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker’s announcement, construction work is deemed ‘essential’ and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates

<https://ahsbuilding.org/news/construction-updates/>

For more information, visit: www.ahsbuilding.org


Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact

Hal Raymond, Skanska Site Representative, (617) 352-8593



PHASE 1 SITEWORK (June 2020 – September 2020)

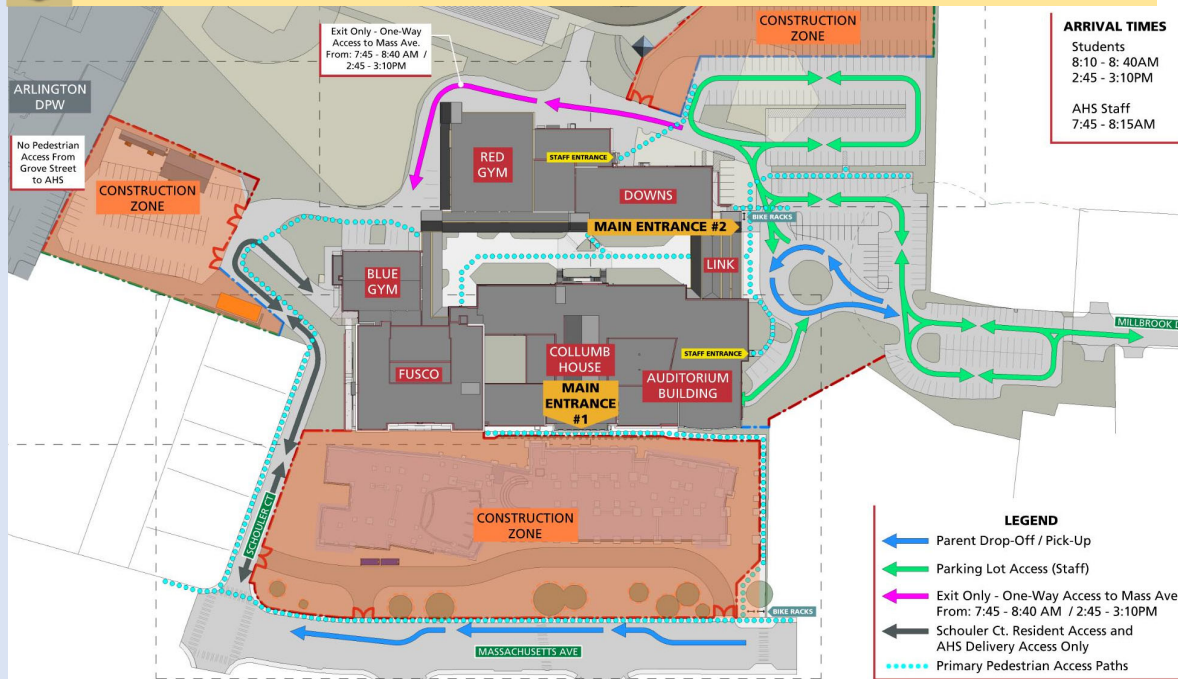

Construction Look Ahead – Week of September 7, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Mass Ave entrance and circular drive closed

General Site Activities

- Mass Ave Front Lawn:
 - Main Entrance #1 pedestrian covered sidewalk preparation
 - Drilling and installation of Rammed Aggregate Piers (RAPs)
 - Start foundations
 - Soil screening and grading
- West Parking Lot:
 - Construction trailers and contractor parking
 - Trenching for installation for electric and telecom services
- Material Stockpile/Temp Construction Lot:
 - Contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site
 - Noise and vibration monitoring during Rammed Aggregate Piers (RAPs) Installation

Weekend Work/Work Hours/Holiday Work

- No work on Labor Day (9/7)
- No weekend work at this time
- Work hours temporarily extended 8:00 am – 6:00 pm (in accordance with local bylaws)



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 7, 2020

Progress Photographs – Taken Week of 08/24/2020



Photograph 1: Installation of overhead protection along the new temporary covered sidewalk



Photograph 2: Spread footings installation for Phase 1 Building



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 7, 2020



Photograph 3: Digging holes for more Phase 1 Building footings



Photograph 4: Installing GCC's for Phase 1 Building



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 7, 2020



Photograph 5: Performing load tests on piers



Photograph 6: View of Phase 1 Site Work in Progress (9/3/20)
