

Arlington High School Building Project

AHS Construction Update - 12/23/20

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details

Phase 1 site-work is complete, and the Phase 1 Building steel is being erected. Work areas during this phase include the front green, the Peirce practice field, and the current softball field. Weekday construction work hours have been temporarily approved for 7AM - 6 PM. Saturday work is required to maintain the schedule. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.


COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement. construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates https://ahsbuilding.org/news/constructi on-updates/ For more information, visit: www.ahsbuilding.org Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

PHASE 1 BUILDING CONSTRUCTION (September 2020 – February 2022)

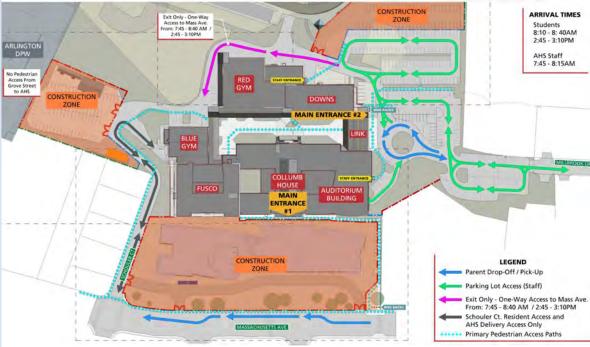

Construction Look Ahead (2-week) -Week of December 24, 2020 & January 4, 2021

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts


- Mass Ave circular drive closed
- Main Entrance #1 covered pedestrian walkway is open

General Site Activities

- Mass Ave Front Lawn:
 - Steel erection
 - Truck deliveries and unloading of steel members
 - Temporary electrical service work
- West Parking Lot:
 - Construction trailers and contractor parking
 - Temporary electrical service work
 - Material Stockpile/Temp Construction Lot:
 - Contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site

Work Hours Update / Weekend Work / Holiday Schedule

- Weekday work hours temporarily extended for a 7AM start time until February 8th, 2021
- There will be no work on New Year's Day 1/1/21
- Saturday work is required until Mid-February 2021









ARLINGTON HIGH SCHOOL

WEEKLY UPDATE - WEEK OF DECEMBER 28, 2020- JANUARY 4,2021

Progress Photographs - Taken Week of 12/14/2020



Photograph 1: Fusco Camera Aerial View of the Site



Photograph 2: Building D Steel Erection progress photo from Mass Ave.



ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF DECEMBER 28, 2020- JANUARY 4,2021



Photograph 2: Building D Steel Erection progress photo
