

# **Arlington High School Building Project**

AHS Construction Update - 9/2/2021

## Arlington HS Construction Schedule: April 2020 – April 2025

#### **Construction Details**


Phase 1 site-work is complete, and Phase 1 building construction is in progress. Work areas during this phase include the front green, the Peirce practice field, and the current softball field. Weekday construction work hours have been temporarily approved for 7AM - 6 PM. Saturday work is required to maintain the schedule. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

#### **COVID-19 Update**

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates https://ahsbuilding.org/news/const ruction-updates/ For more information, visit: www.ahsbuilding.org Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hall Raymond, Skanska Site Representative, (617) 352-8593

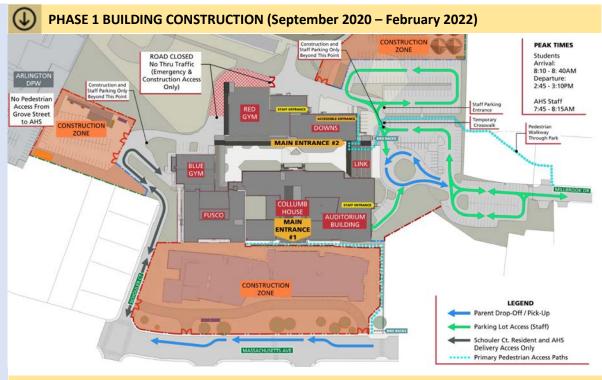

### Construction Look Ahead – Week of September 6th, 2021

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

### **Public Way Impacts**

- Mass Ave circular drive closed
- Main Entrance #1 covered pedestrian walkway is open

#### **General Site Activities:**

- Mass Ave Front Lawn:
  - Interior framing
  - Interior paint
  - Fire protection installation
  - Exterior brick installation
  - Exterior window Installation
  - HVAC units install on roof top
- West Parking Lot:
  - Construction trailers and contractor parking
- Material Stockpile/Temp Construction Lot:
  - Contractor storage and parking
- **Schouler Court:** 
  - Construction vehicles entering and exiting project site

### Weekend Work / Holiday Work

- Site is closed on Labor Day, 9/6/2021
- Saturday work is required for the foreseeable future









## **ARLINGTON HIGH SCHOOL**

# WEEKLY UPDATE - WEEK OF SEPTEMBER 6TH, 2021

Progress Photographs - Taken Week of 09/03/2021



Photograph 1: Building D/E South Elevation (Main Entrance)



Photograph 2: Building D South Elevation



# **ARLINGTON HIGH SCHOOL**

# WEEKLY UPDATE – WEEK OF SEPTEMBER 6<sup>TH</sup>, 2021



Photograph 3: Building D East Elevation



Photograph 4: Building E West Elevation (Schouler Ct)
