



Arlington High School Building Project

AHS Construction Update – 9/16/2021

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details

Phase 1 site-work is complete, and Phase 1 building construction is in progress. Work areas during this phase include the front green, the Peirce practice field, and the current softball field. Weekday construction work hours have been temporarily approved for 7AM – 6 PM. Saturday work is required to maintain the schedule. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.


COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
For more information, visit:
www.ahsbuilding.org
Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

PHASE 1 BUILDING CONSTRUCTION (September 2020 – February 2022)

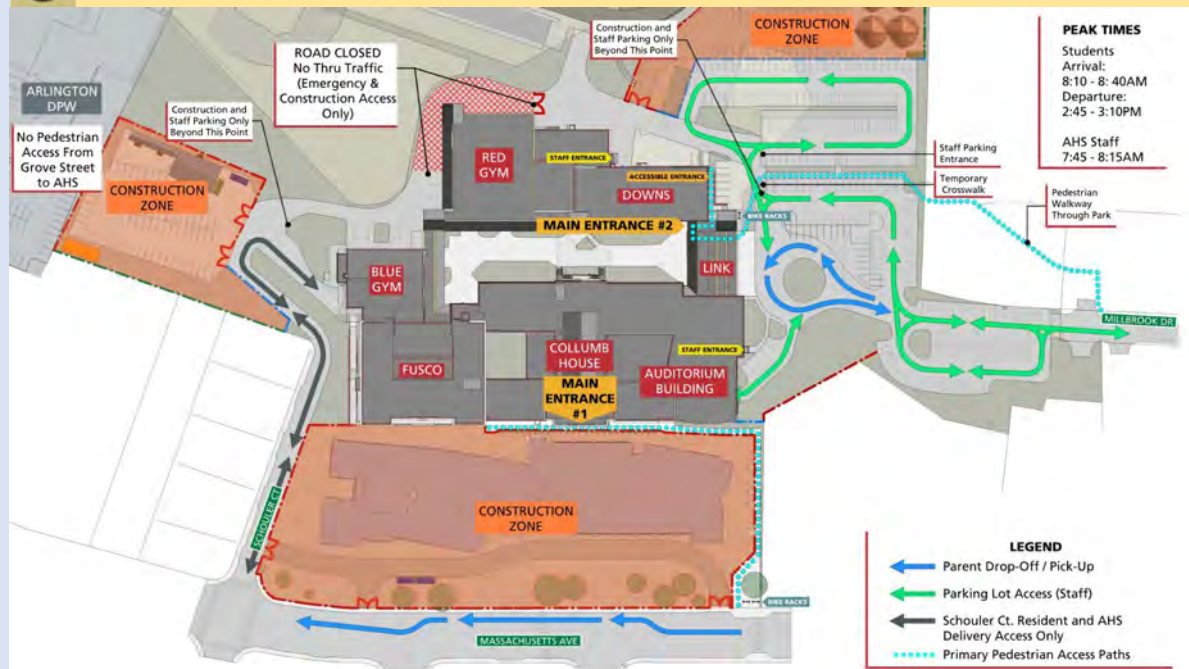

Construction Look Ahead – Week of September 20th, 2021

For questions about the start of the school year, refer to the [Student Quick Guide](#)

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Mass Ave circular drive closed
- Main Entrance #1 covered pedestrian walkway is open

General Site Activities:

- Mass Ave Front Lawn:
 - Interior framing
 - Interior paint
 - Fire protection installation
 - Exterior brick installation
 - Exterior window installation
 - Roof top mechanical equipment installation
- West Parking Lot:
 - Construction trailers and contractor parking
- Material Stockpile/Temp Construction Lot:
 - Contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site
 - Crane work on West side of site on Monday 9/20/2021

Weekend Work / Holiday Work

- Saturday work is required for the foreseeable future



ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 20TH, 2021

Progress Photographs – Taken Week of 09/13/2021



Photograph 1: Building D/E South Elevation (Mass Ave)



Photograph 2: Building D East Elevation



ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 20TH, 2021



Photograph 3: Building D South Elevation (Mass Ave)



Photograph 4: Building E West Elevation (Schouler Court)
