



Arlington High School Building Project

AHS Construction Update – February 02, 2023


Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

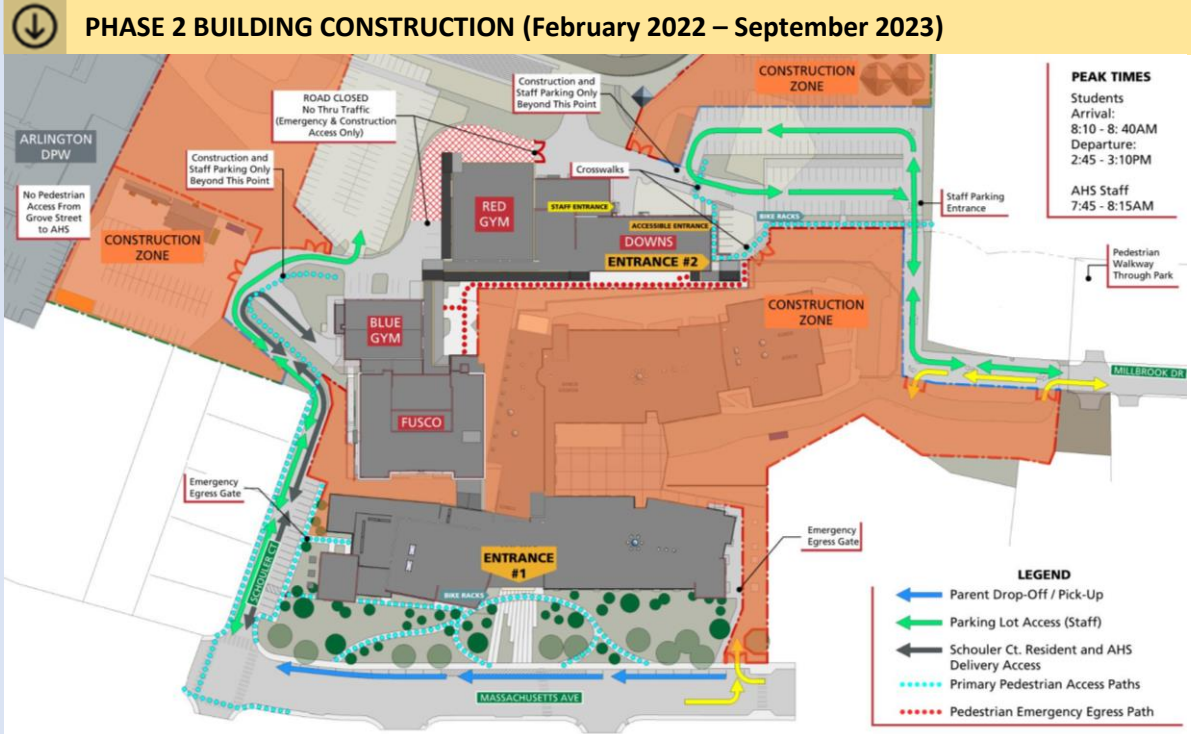

Construction Look Ahead – Week of February 6th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Phase 2:
 - Concrete placement
 - Steel fireproofing
 - Install skylights
 - Installation of stairwells
 - Layout for overhead M/E/P and corridor framing
 - Installation of roofing system
 - Install temporary tarp around building for winter conditions
 - Install CMU of elevator shaft
 - Dust mitigation ongoing

- Material Stockpile/Temp Construction Lot:

- Contractor storage and parking

- Schouler Court:

- Construction vehicles entering and exiting project site

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF FEBRUARY 6TH, 2023

Progress Photographs – Taken Week of 1/30/2023.



Photograph 1: Phase 2 East Elevation (Mill Brook Dr)



Photograph 2: Concrete placement in progress



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF FEBRUARY 6TH, 2023



Photograph 3: Central Spine Forum Stair Progress
