

Arlington High School Building Project

AHS Construction Update - March 9, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.


COVID-19 Update

The health and safety of the community and workers onsite are of the highest priority and were taken into consideration in all projectrelated decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly **Construction Updates** https://ahsbuilding.org/news/c onstruction-updates/ For more information, visit: www.ahsbuilding.org Email questions or concerns to:

ahsbuilding@arlington.k12.ma

.us For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

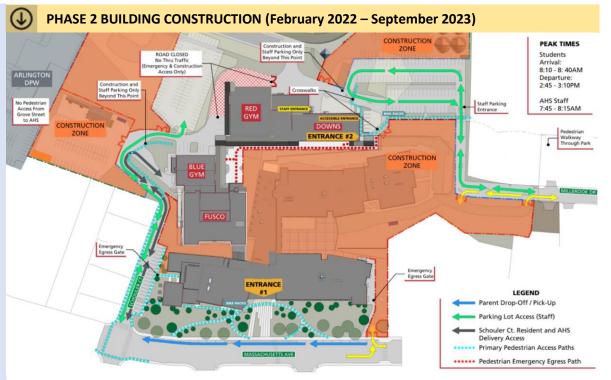

Construction Look Ahead – Week of March 13th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

• **Deliveries ongoing**

General Site Activities:

- Phase 2:
 - Steel fireproofing 0
 - Steel detailing 0
 - Concrete placement 0
 - Installation of curtain wall 0
 - Exterior and interior framing 0
 - Install mechanical, electrical, plumbing, and fire sprinklers 0
 - Installation of roofing system 0
 - Installation of elevator shaft 0
 - Dust mitigation ongoing
- Material Stockpile/Temp Construction Lot:
 - Contractor storage and parking
 - Schouler Court:
 - Construction vehicles entering and exiting project site

Weekend Work/Holiday Work/Night Work:

Saturday work is required for the foreseeable future

SKANSKA





HMFH Architects, Inc Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF MARCH 13TH, 2023



View of connector from Building D to Building B, Building B and partial of Building C

ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF MARCH 13TH, 2023




Progress of Main Entrance


Progress of interior framing and overhead mechanical and fire sprinkler



ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF MARCH 13TH, 2023

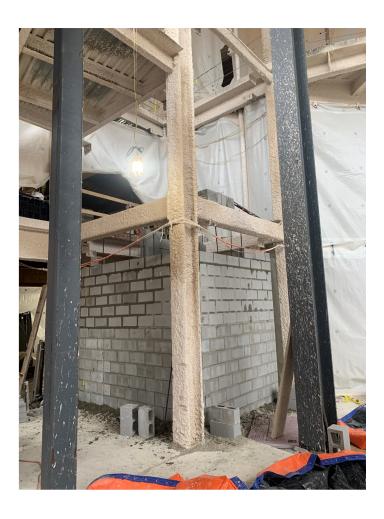

Progress of elevator shaft

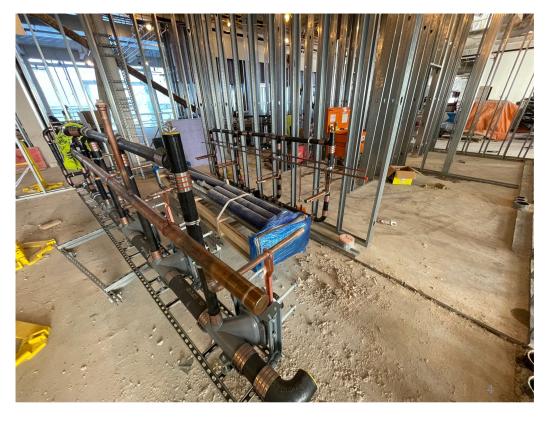

Piping for bathroom fixtures getting assembled
