

Arlington High School Building Project

AHS Construction Update – August 17th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers onsite are of the highest priority and were taken into consideration in all projectrelated decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates https://ahsbuilding.org/news/c onstruction-updates/ For more information, visit: www.ahsbuilding.org Email questions or concerns to: ahsbuilding@arlington.k12.ma

.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



Construction Look Ahead - Week of August 21st, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

Deliveries ongoing

General Site Activities:

- Phase 2:
 - Installation of masonry
 - Installation of framing, drywall and painting
 - Installation of ceramic wall tiles, epoxy terrazzo flooring and carpet
 - Installation of ceiling grids and ceiling tiles
 - Installation of door frames, interior windows, and casework
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinklers
 - Installation of fixtures
 - Start-up and testing of mechanical units
 - Grading of exterior site
 - Install of permanent Retaining Wall
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- **Schouler Court:**
 - Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:


Saturday work is required for the foreseeable future






ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF AUGUST 21ST, 2023

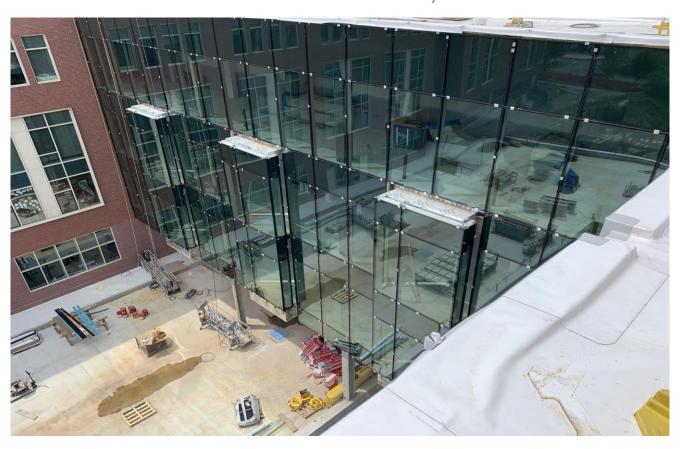

Photograph 1: Phase 2 Courtyard area curtainwall install

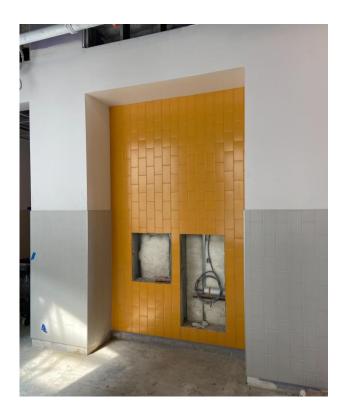

Photograph 2: Accent Tile outside Corridor Bathrooms



Photograph 3: Level 1 Mechanical Room

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF AUGUST 21ST, 2023



Photograph 4: Phase 2 East Elevation (Mill Brook Dr)
