

Arlington High School Building Project

AHS Construction Update – October 26th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

COVID-19 Update


The health and safety of the community and workers onsite are of the highest priority and were taken into consideration in all projectrelated decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates <u>https://ahsbuilding.org/news/construction-updates/</u> For more information, visit: <u>www.ahsbuilding.org</u> Email questions or concerns to:

ahsbuilding@arlington.k12.ma

<u>.us</u>

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

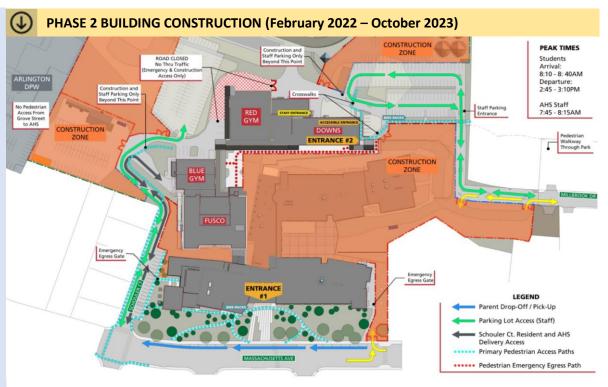

Construction Look Ahead – Week of October 30th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

Deliveries ongoing

General Site Activities:

- Phase 2:
 - Installation of masonry
 - Painting and final cleaning.
 - o Delivery and installation of display boards and furniture.
 - Installation of ceiling grids and ceiling tiles
 - Installation of casework
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinklers.
 - o Installation of plumbing and electrical fixtures
 - Start-up and testing of mechanical units.
 - Grading of exterior site and loading dock area
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

Saturday work is required for the foreseeable future.





HMFH Architects, Inc Architect

ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF OCTOBER 30TH, 2023



Photograph 1: Progress of appliance install.



Photograph 2: East Elevation (Mill Brook Dr)
