

Arlington High School Building Project

AHS Construction Update – November 9th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 construction is nearly complete, and the new Humanities classroom wing and district offices are open. Menotomy Preschool is expected to be complete in December. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.


COVID-19 Update

The health and safety of the community and workers onsite are of the highest priority and were taken into consideration in all projectrelated decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our

Sign up for Weekly Construction Updates https://ahsbuilding.org/news/c onstruction-updates/ For more information, visit: www.ahsbuilding.org Email questions or concerns to: ahsbuilding@arlington.k12.ma

.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

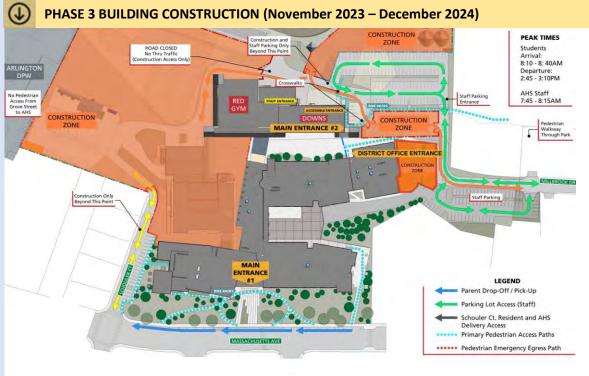

Construction Look Ahead – Week of November 13th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

Deliveries ongoing

General Site Activities:

- Phase 2:
 - Installation of masonry
 - Landscaping
 - Pre-School
 - Installation of flooring and ceiling
 - Installation of casework
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinklers.
- Phase 3:
 - Start Fusco Link Abatement
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

Saturday work is required for the foreseeable future.

SKANSKA S

Skanska USA Inc. Owner's Project Manager




Consigli Construction Co., Inc. Onstruction Manager at Risk




HMFH Architects, Inc Architect

ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF NOVEMBER 13TH, 2023

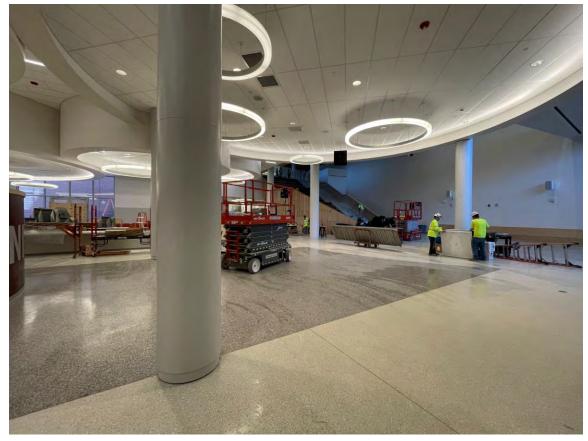


Photograph 1: Final Clean of Cafeteria Area

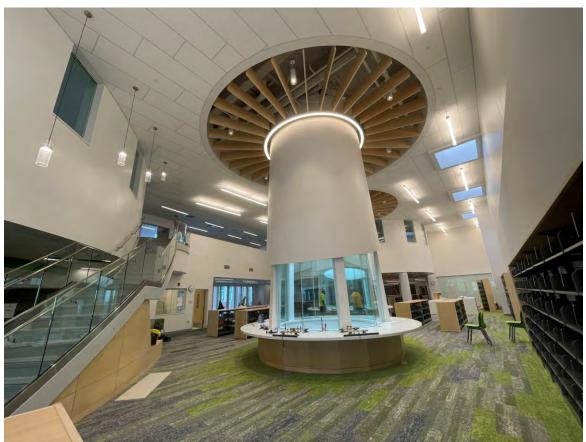

Photograph 2: Library

ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF NOVEMBER 13TH, 2023

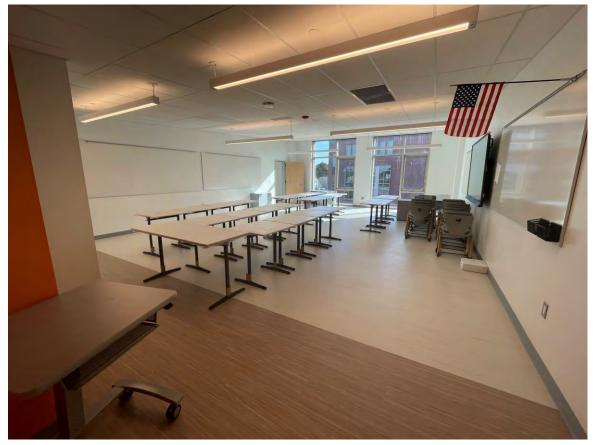

Photograph 3: Classroom Furniture Delivery



Photograph 4: East Elevation (Mill Brook Dr)
