



Arlington High School Building Project

AHS Construction Update – November 30th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 construction is nearly complete, and the new Humanities classroom wing and district offices are open. Menotomy Preschool is expected to be complete in December. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.


COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our

Sign up for Weekly Construction Updates <https://ahsbuilding.org/news/construction-updates/>
For more information, visit: www.ahsbuilding.org
Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

PHASE 3 BUILDING CONSTRUCTION (November 2023 – December 2024)

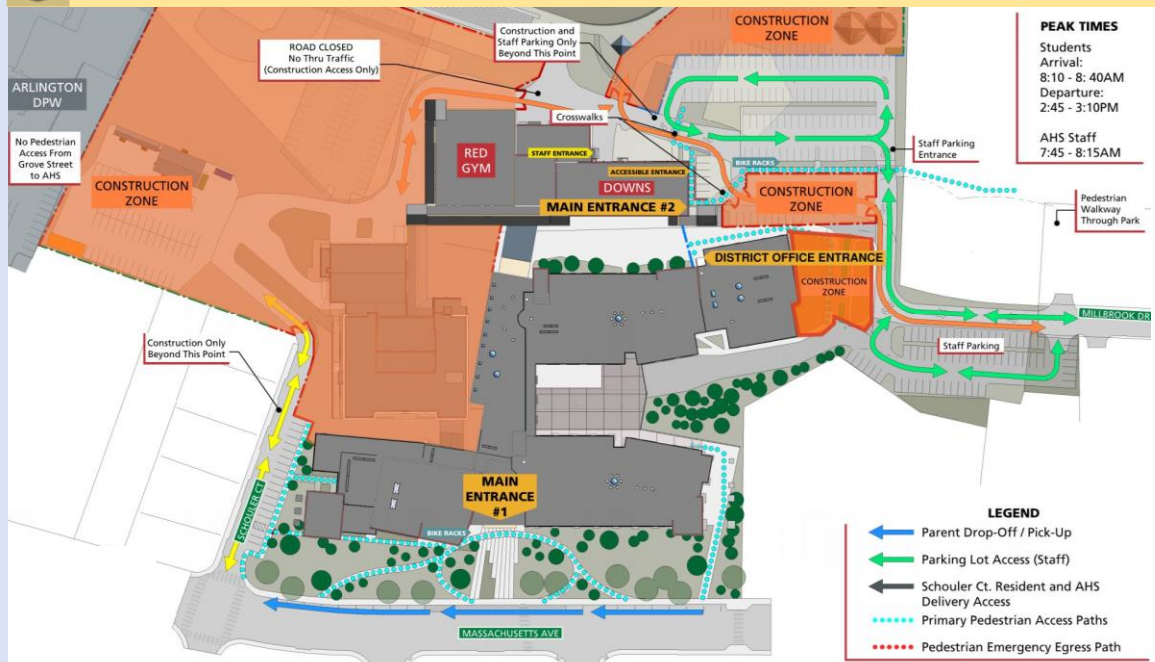

Construction Look Ahead – Week of December 4th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Phase 2:
 - Installation of masonry
 - Landscaping
 - Pre-School
 - Installation of flooring and ceiling
 - Installation of casework
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinklers.
- Phase 3:
 - Abatement of Fusco
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.



Skanska USA Inc.
Owner's Project Manager



Consigli Construction Co., Inc.
Construction Manager at Risk




HMFH Architects, Inc.
Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF DECEMBER 4TH, 2023



Photograph 1: Pre-School Multipurpose Room

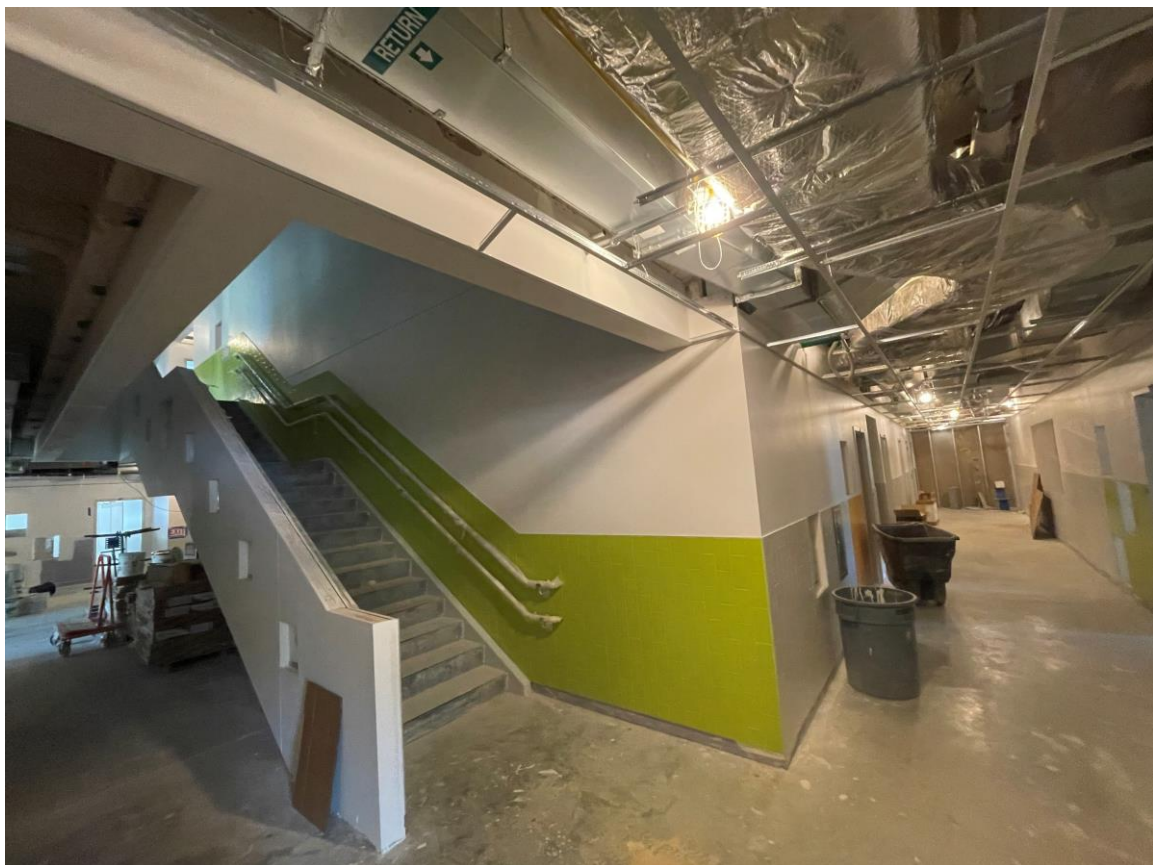

Photograph 2: Pre-School Corridor Progress

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF DECEMBER 4TH, 2023



Photograph 3: Pre-School and Daycare sitework progress



Photograph 4: East Elevation (Mill Brook Dr)
