




Arlington High School Building Project

AHS Construction Update – December 7th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025



PHASE 3 BUILDING CONSTRUCTION (November 2023 – December 2024)

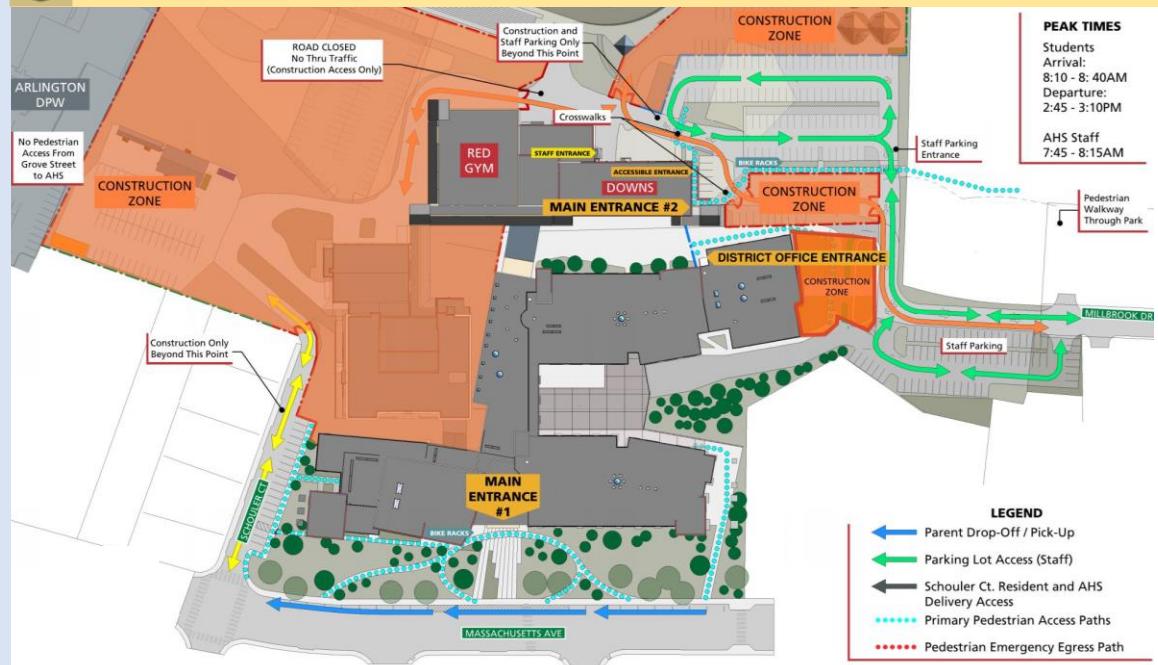

PEAK TIMES

Students
 Arrival: 8:10 - 8:40AM
 Departure: 2:45 - 3:10PM
 AHS Staff
 7:45 - 8:15AM

LEGEND

- Parent Drop-Off / Pick-Up
- Parking Lot Access (Staff)
- Schouler Ct. Resident and AHS Delivery Access
- Primary Pedestrian Access Paths
- Pedestrian Emergency Egress Path

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 construction is nearly complete, and the new Humanities classroom wing and district offices are open. Menotomy Preschool is expected to be complete in December. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our

Construction Look Ahead – Week of December 11th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Phase 2:
 - Landscaping
 - Pre-School
 - Installation of flooring and ceiling
 - Installation of casework
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinkler fixtures.
- Phase 3:
 - Start Fusco Link Abatement
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



Skanska USA Inc.
 Owner's Project Manager



Consigli Construction Co., Inc.
 Construction Manager at Risk



HMFH Architects, Inc.
 Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF DECEMBER 11TH, 2023



Photograph 1: Pre-School Playground structure progress.



Photograph 2: Pre-School Playground structure progress.

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF DECEMBER 11TH, 2023



Photograph 3: Pre-School and Daycare bathroom fixtures progress.



Photograph 4: Phase 2 East Elevation (Mill Brook Dr).
