



Arlington High School Building Project

AHS Construction Update – April 11th, 2024


Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

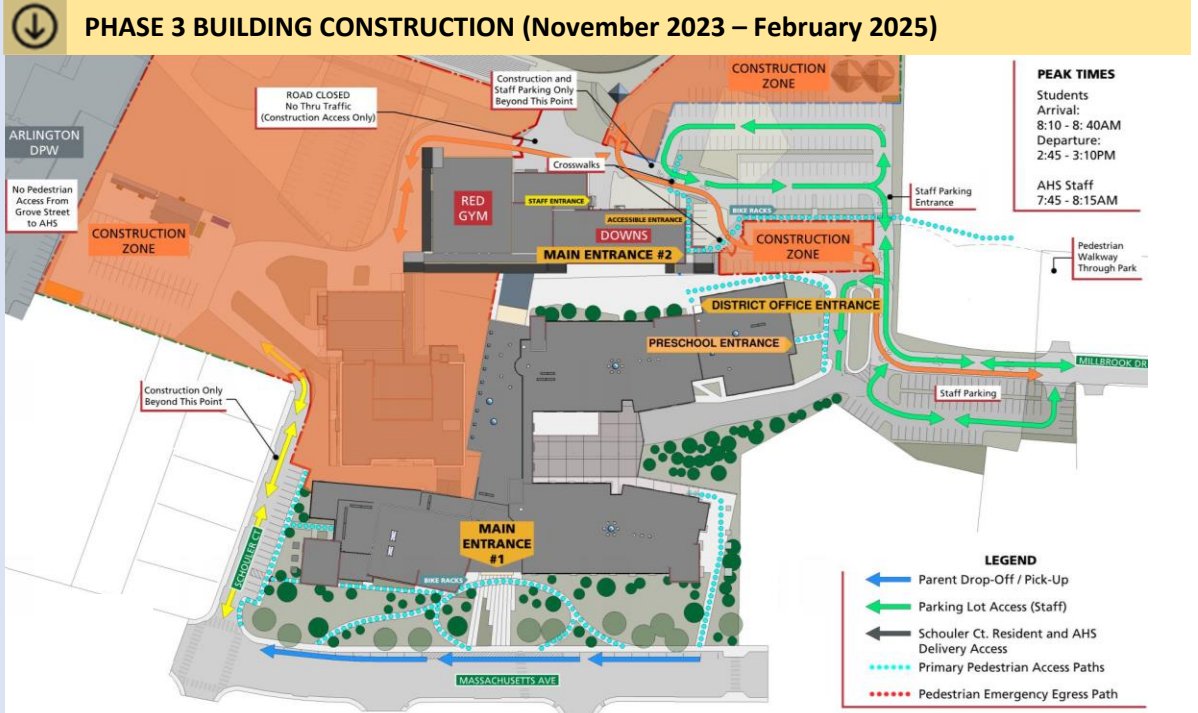

Construction Look Ahead – Week of April 15th, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Continue formwork of footings in preparation for concrete pour.
- Continue coordinating concrete pour of footings.
- Sitework for Minuteman Bike Path
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Continue underground plumbing and electrical work
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

ARLINGTON HIGH SCHOOL
WEEKLY UPDATE – WEEK OF APRIL 15TH 2024



Photograph 1: Grade beams rebar tie-in and formwork.



Photograph 2: Concrete pour of grade beams & pile caps.

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF APRIL 15TH 2024



Photograph 3: Phase 3 West Elevation (Scholuer Ct)
