



Arlington High School Building Project

AHS Construction Update – June 6th, 2024


Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

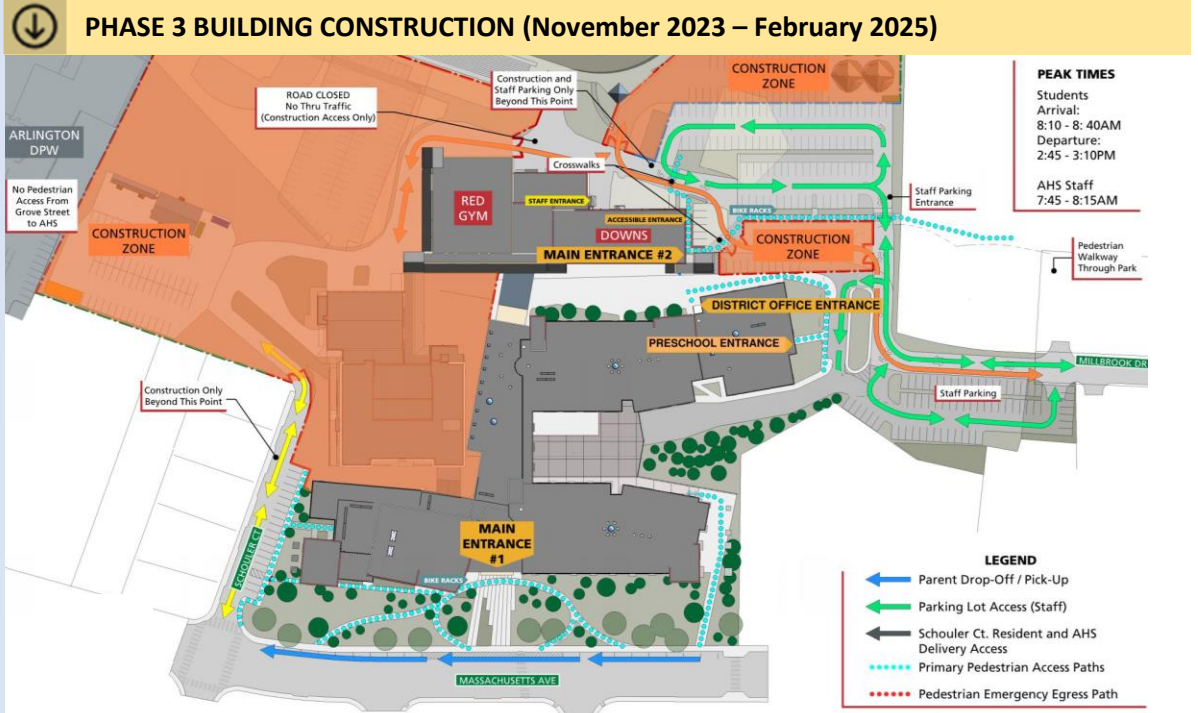

Construction Look Ahead – Week of June 10th, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Complete steel erection of Building A, continue structural deck and detailing.
- Coordinate concrete slab placement of Building A.
- Place Toilet Facility Building concrete slab
- Sitework for Minuteman Bike Path and ramp.
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



Skanska USA Inc.
 Owner's Project Manager



Consigli Construction Co., Inc.
 Construction Manager at Risk



HMFH Architects, Inc.
 Architect

ARLINGTON HIGH SCHOOL
WEEKLY UPDATE – WEEK OF JUNE 10TH ,2024



Photograph 1: Elevation of Level 1 structural erection.



Photograph 2: Elevation of level 2 and roof truss structural steel erection.

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JUNE 10TH ,2024



Photograph 3: Toilet Building Facility underground Plumbing and Electrical Rough.



Photograph 4: West Elevation (Schouler Ct)
