



Arlington High School Building Project

AHS Construction Update – June 27th, 2024


Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

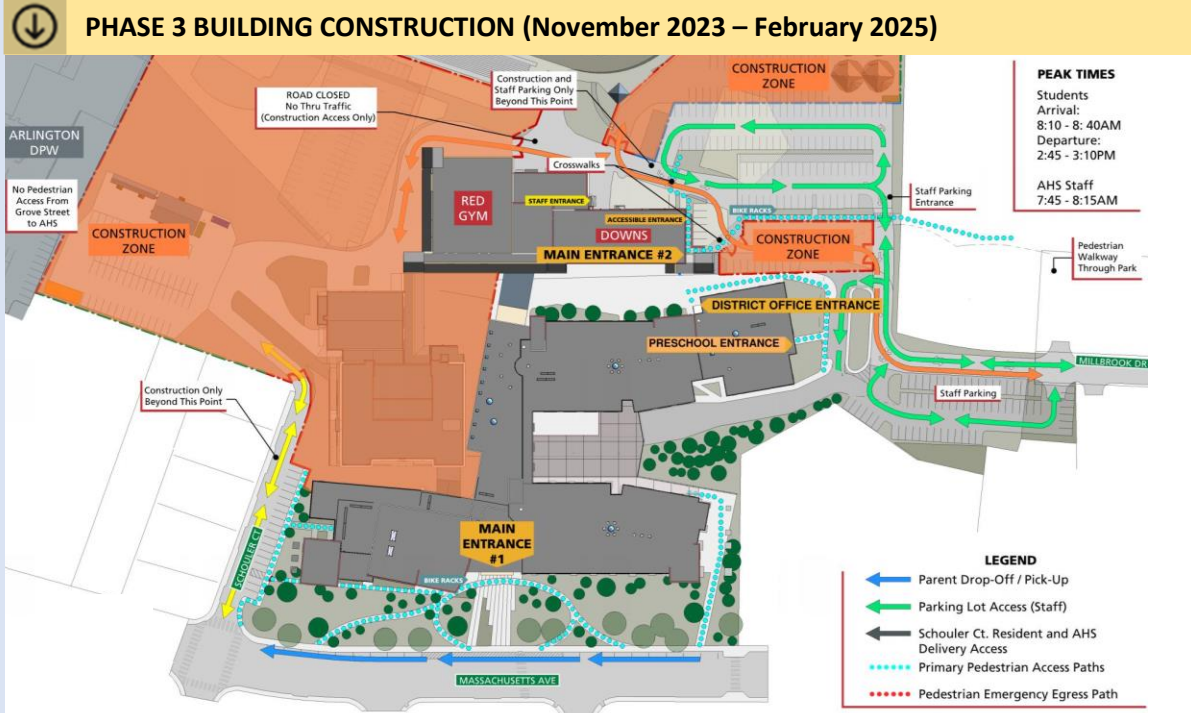

Construction Look Ahead – Week of July 1st, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Continue structural deck and detailing.
- Install Toilet Facility Building exterior masonry walls.
- Continue sitework for Minuteman Bike Path and ramp.
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.
- Continue spray fireproofing of level 2.
- Install exterior landscape and pavers at courtyard plaza.
- Curb and sidewalk installation around preschool and Millbrook Drive.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.
- In observance of July 4th, site is closed.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



Skanska USA Inc.
 Owner's Project Manager



Consigli Construction Co., Inc.
 Construction Manager at Risk



HMFH Architects, Inc.
 Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JULY 1ST ,2024



Photograph 1: Aerial View of Project



Photograph 2: West Elevation (Schouler Ct)
