

Arlington High School Building Project

AHS Construction Update - July 11th, 2024

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details


Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers onsite are of the highest priority and were taken into consideration in all projectrelated decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly
Construction Updates
https://ahsbuilding.org/news/construction-updates/
For more information, visit:
www.ahsbuilding.org
Email questions or
concerns to:
ahsbuilding@arlington.k12.ma
.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

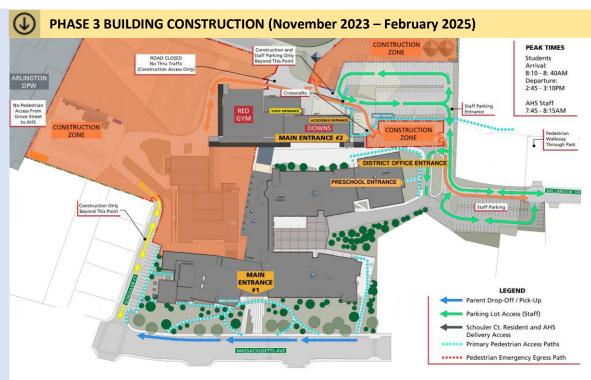

Construction Look Ahead – Week of July 15th, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

Deliveries ongoing

General Site Activities:

- Continue backfilling Level 1 structural slab on grade and setup for rebar install.
- Continue perimeter framing on North Elevation of Building A.
- Continue Toilet Facility Building block masonry walls.
- Continue sitework for Minuteman Bike Path and ramp.
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Continue spray fireproofing of level 2.
- Millbrook Drive and Mill Street intersection signal work to continue.
- Curb and sidewalk installation around preschool and Millbrook Drive.
- Schouler Court:
 - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

Saturday work is required for the foreseeable future.





ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF JULY 15TH ,2024



Photograph 1: Aerial View of Building A footprint.



Photograph 2: Level 2 rebar install.

ARLINGTON HIGH SCHOOL WEEKLY UPDATE – WEEK OF JULY 15TH ,2024



Photograph 3: Aerial View of Bike Path Progress

