



# Arlington High School Building Project

AHS Construction Update – July 18<sup>th</sup>, 2024


## Arlington HS Construction Schedule: April 2020 – September 2025

### Construction Details

Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

### COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

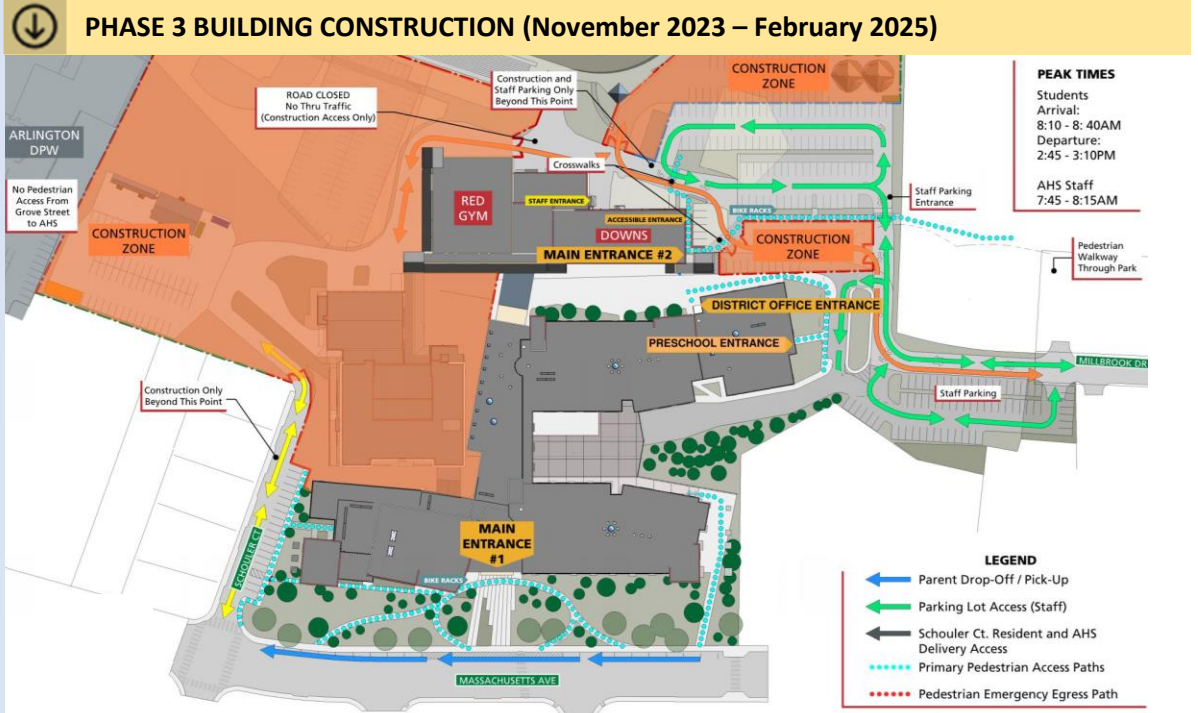

### Construction Look Ahead – Week of July 22<sup>nd</sup>, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts:

- Deliveries ongoing

#### General Site Activities:

- Continue backfilling, installing rebar on Level 1 structural slab on grade and prep for concrete pour. Concrete placement to take place 7/29 with heavy traffic of trucks entering and exiting the site through Schouler Court.
- Continue installation of perimeter framing, sheathing and AVB on Building A.
- Install roof of Toilet Facility Building.
- Continue sitework for Minuteman Bike Path and ramp.
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Complete Millbrook Drive and Mill Street intersection signal work.
- Curb and sidewalk installation around preschool and Millbrook Drive.
- Continue installing pavers and planters in the courtyard plaza.
- Schouler Court:
  - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

#### Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.

Sign up for Weekly Construction Updates  
<https://ahsbuilding.org/news/construction-updates/>  
 For more information, visit:  
[www.ahsbuilding.org](http://www.ahsbuilding.org)  
 Email questions or concerns to:  
[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



Skanska USA Inc.  
 Owner's Project Manager



Consigli Construction Co., Inc.  
 Construction Manager at Risk



HMFH Architects, Inc.  
 Architect

# ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JULY 22<sup>ND</sup> ,2024



***Photograph 1: West Elevation (Schouler Ct)***
