

## **Arlington High School Building Project**

AHS Construction Update – September 5<sup>th</sup>, 2024

## Arlington HS Construction Schedule: April 2020 – September 2025

#### **Construction Details**

Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.


#### **COVID-19 Update**

The health and safety of the community and workers onsite are of the highest priority and were taken into consideration in all projectrelated decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly
Construction Updates
<a href="https://ahsbuilding.org/news/construction-updates/">https://ahsbuilding.org/news/construction-updates/</a>
For more information, visit:
<a href="https://www.ahsbuilding.org">www.ahsbuilding.org</a>
Email questions or
concerns to:

ahsbuilding@arlington.k12.ma .us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

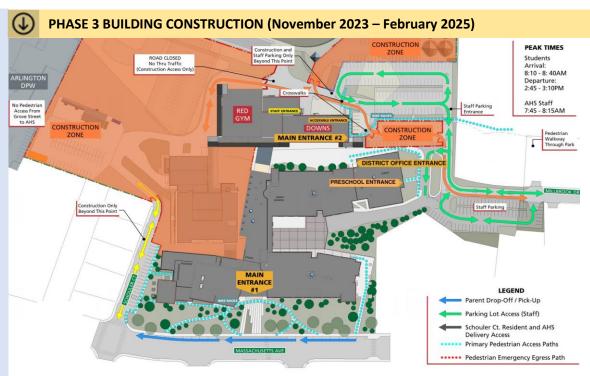

### Construction Look Ahead – Week of September 9th, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

### **Public Way Impacts:**

- Deliveries ongoing
- Traffic light on Mill Street and Millbrook Drive is activated and in flashing mode until 9/18/24 when it will be in full operation.

#### **General Site Activities:**

- Continue installation of exterior framing, sheathing and curtainwall installation
- Continue interior framing and drywall
- Installation of mechanical, plumbing, and electrical systems
- Continue installing pavers and planters in the courtyard plaza
- Concrete work on the Minuteman Bike Path and ramp.
- Commence exterior block on the Toilet Facility Building
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
  - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

## Weekend Work/Holiday Work/Night Work:

Saturday work is required for the foreseeable future.





## **ARLINGTON HIGH SCHOOL**

# WEEKLY UPDATE – WEEK OF SEPTEMBER 9<sup>TH</sup>,2024




Photograph 1: Level 2 interior framing hallway progress.



Photograph 2: Level 2 interior framing gym progress.

## **ARLINGTON HIGH SCHOOL**

## WEEKLY UPDATE – WEEK OF SEPTEMBER 9<sup>TH</sup>,2024

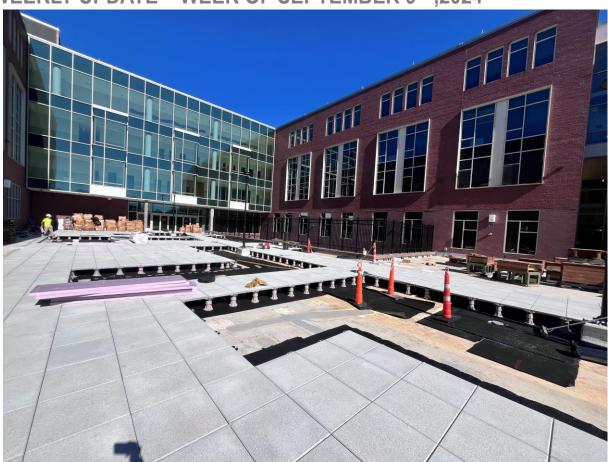

Photograph 3: Exterior Courtyard Plaza paver installation progress.



Photograph 4: West Elevation (Schouler Ct).
